


eParts Intelligent Ingestion & Attribute Prediction Platform — WBS Overview

Team: Pimsie Supreme | CMU MSE Studio Capstone | Jan 22 – Dec 11, 2026

Legend: Completed In Progress Future Work

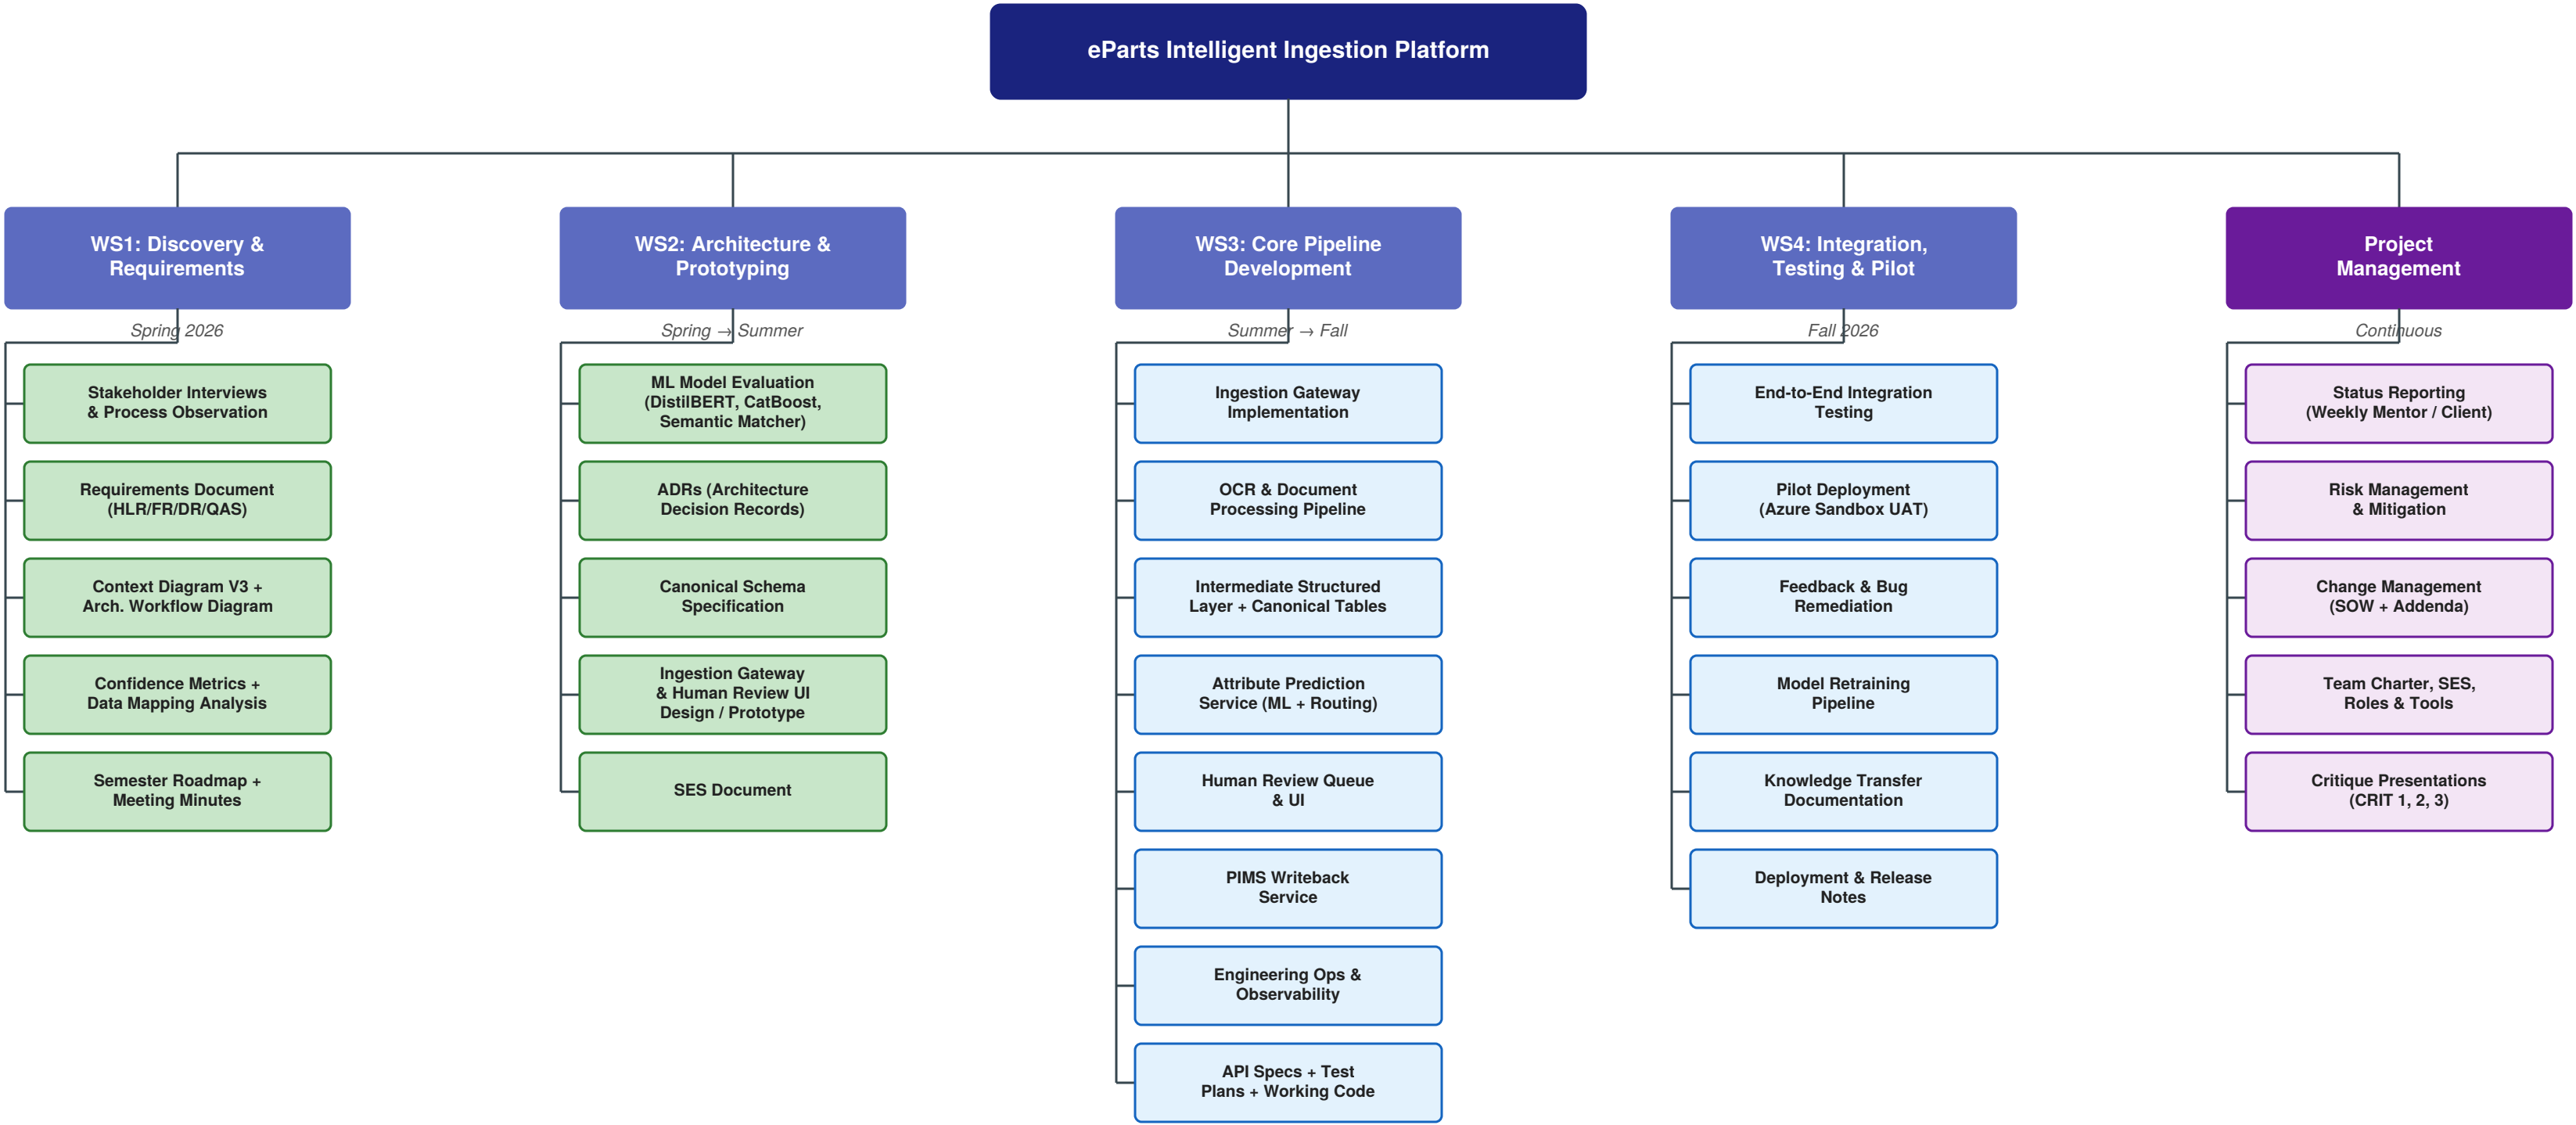

Project Timeline (Spring → Summer → Fall 2026)


| Spring 2026<br>Jan 22 – May 11         |                                       |                                                                   |                                                                |                                                 | Summer 2026<br>May 18 – Aug 8           |                                                   |                                                   | Fall 2026<br>Aug 24 – Dec 11                    |                                                  |                                        |                                                |                                        |
|----------------------------------------|---------------------------------------|-------------------------------------------------------------------|----------------------------------------------------------------|-------------------------------------------------|-----------------------------------------|---------------------------------------------------|---------------------------------------------------|-------------------------------------------------|--------------------------------------------------|----------------------------------------|------------------------------------------------|----------------------------------------|
| P1: Discovery + SES<br>Feb 18 – Feb 27 | P2: Reqs + Arch v1<br>Feb 28 – Mar 17 | P3: Vertical Slice 1<br>Ingestion → Normalized<br>Mar 18 – Mar 31 | P4: Vertical Slice 2<br>Prediction + Routing<br>Apr 1 – Apr 14 | P5: Hardening + Critique Demo<br>Apr 15 – May 1 | P6: Wrap + Evaluations<br>May 2 – May 4 | Core Pipeline Development (WS3)<br>Full Build-Out | ML Service + Integrations<br>Attribute Prediction | CRIT 2: Summer End-of-Semester<br>End of Summer | Integration + E2E Testing (WS4)<br>Full Pipeline | Pilot Deployment (UAT)<br>Sandbox Env. | Knowledge Transfer + Handoff<br>Final Delivery | CRIT 3: Final Delivery<br>Dec 11, 2026 |

WBS based on deliverable-oriented decomposition (Workstreams 1–4 from SOW v2 + Project Management).

WS1 — Discovery & Requirements Engineering

Spring 2026 (Jan 22 – May 4) · Status: Mostly Completed

Legend: Completed In Progress Future Work

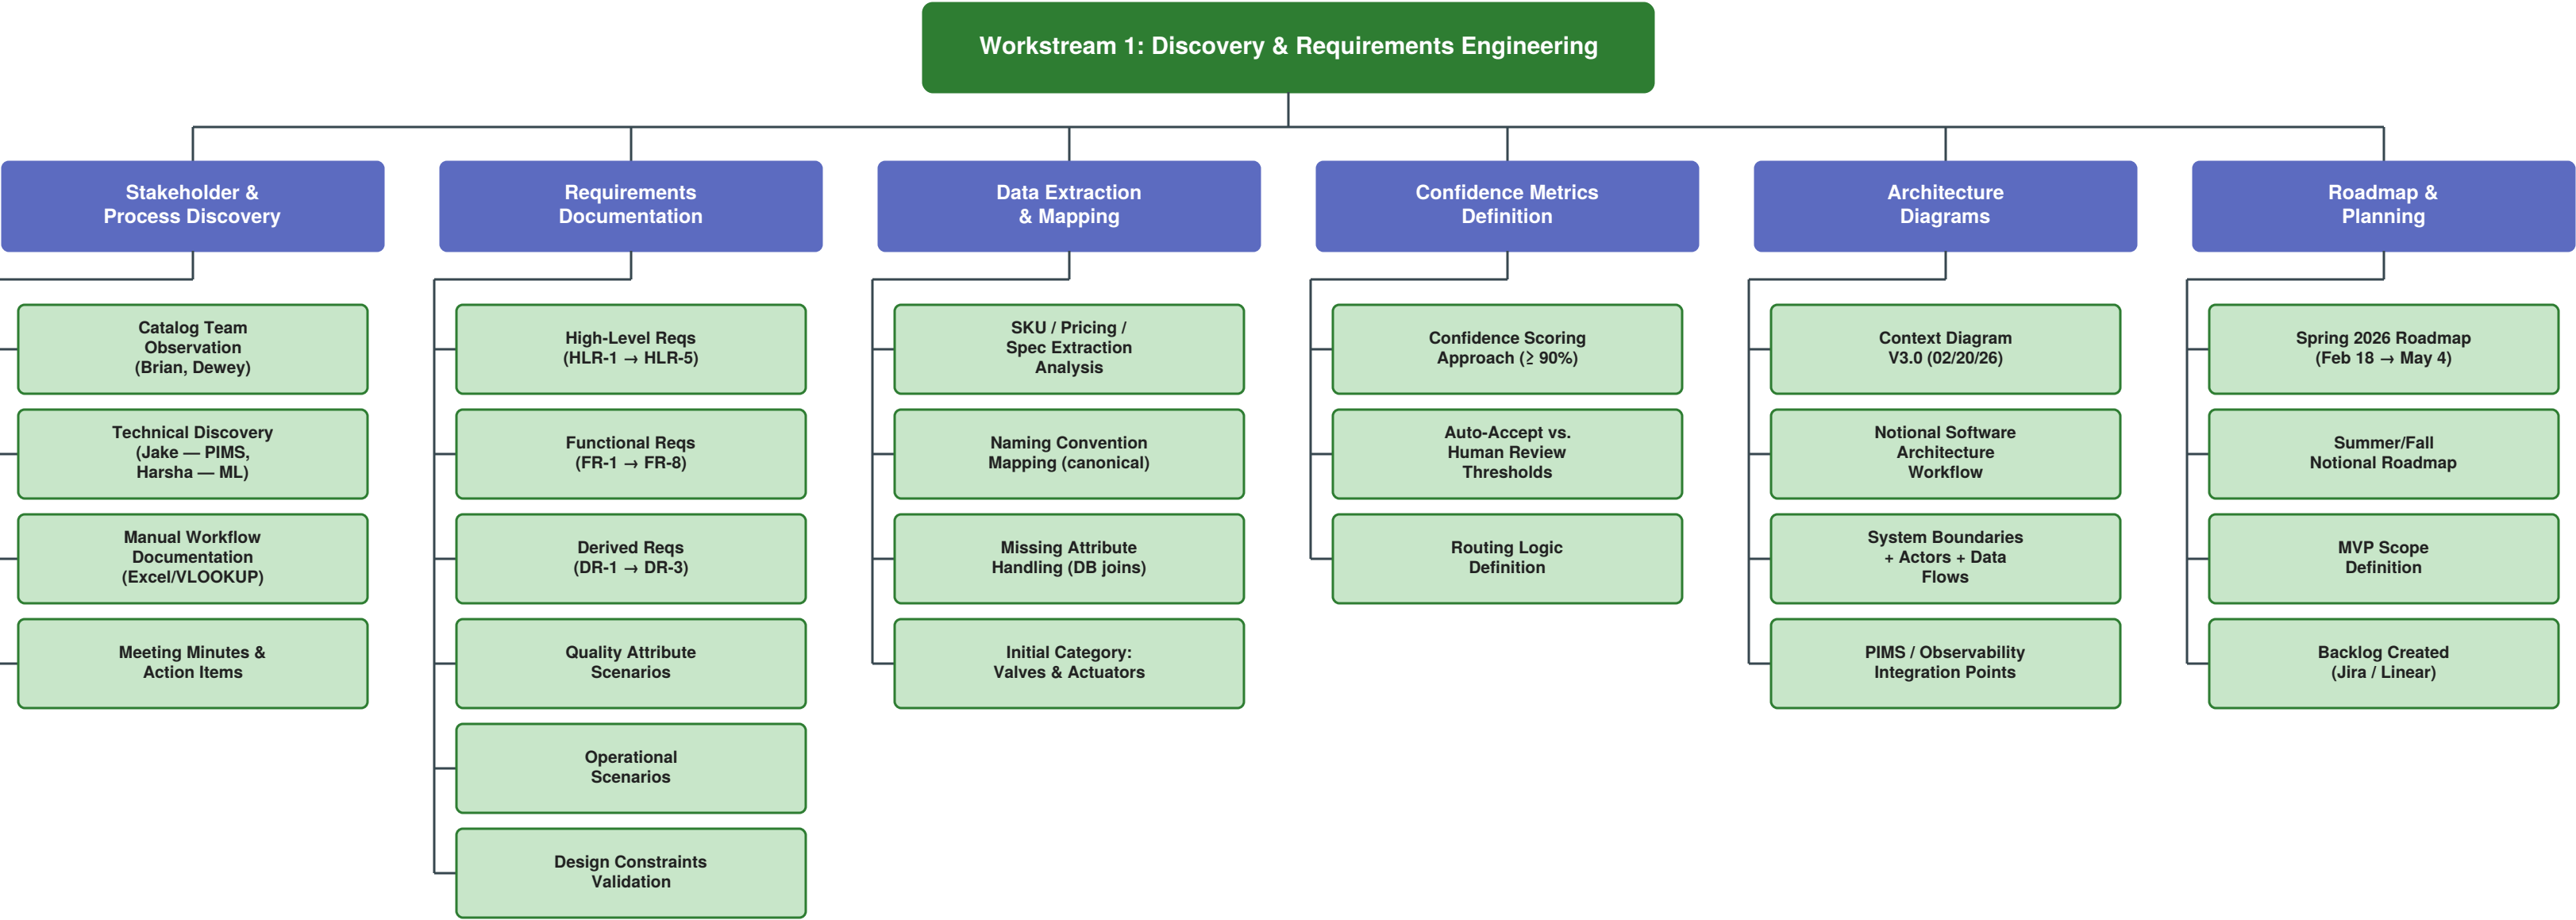

Project Timeline — context for this workstream


| Spring 2026<br>Jan 22 – May 11         |                                       |                                                                   |                                                                |                                                 | Summer 2026<br>May 18 – Aug 8           |                                                   |                                                   |                                                 | Fall 2026<br>Aug 24 – Dec 11                     |                                        |                                                |                                        |
|----------------------------------------|---------------------------------------|-------------------------------------------------------------------|----------------------------------------------------------------|-------------------------------------------------|-----------------------------------------|---------------------------------------------------|---------------------------------------------------|-------------------------------------------------|--------------------------------------------------|----------------------------------------|------------------------------------------------|----------------------------------------|
| P1: Discovery + SES<br>Feb 18 – Feb 27 | P2: Reqs + Arch v1<br>Feb 28 – Mar 17 | P3: Vertical Slice 1<br>Ingestion → Normalized<br>Mar 18 – Mar 31 | P4: Vertical Slice 2<br>Prediction + Routing<br>Apr 1 – Apr 14 | P5: Hardening + Critique Demo<br>Apr 15 – May 1 | P6: Wrap + Evaluations<br>May 2 – May 4 | Core Pipeline Development (WS3)<br>Full Build-Out | ML Service + Integrations<br>Attribute Prediction | CRIT 2: Summer End-of-Semester<br>End of Summer | Integration + E2E Testing (WS4)<br>Full Pipeline | Pilot Deployment (UAT)<br>Sandbox Env. | Knowledge Transfer + Handoff<br>Final Delivery | CRIT 3: Final Delivery<br>Dec 11, 2026 |

WS1 corresponds to Spring 2026 Phases P1–P2 in the roadmap. All deliverables in this workstream are completed and baselined.

WS2 — Architecture & Prototyping

Spring 2026 → Summer 2026 · Status: Spring portion complete; Summer portion in progress / upcoming

Legend: Completed In Progress Future Work

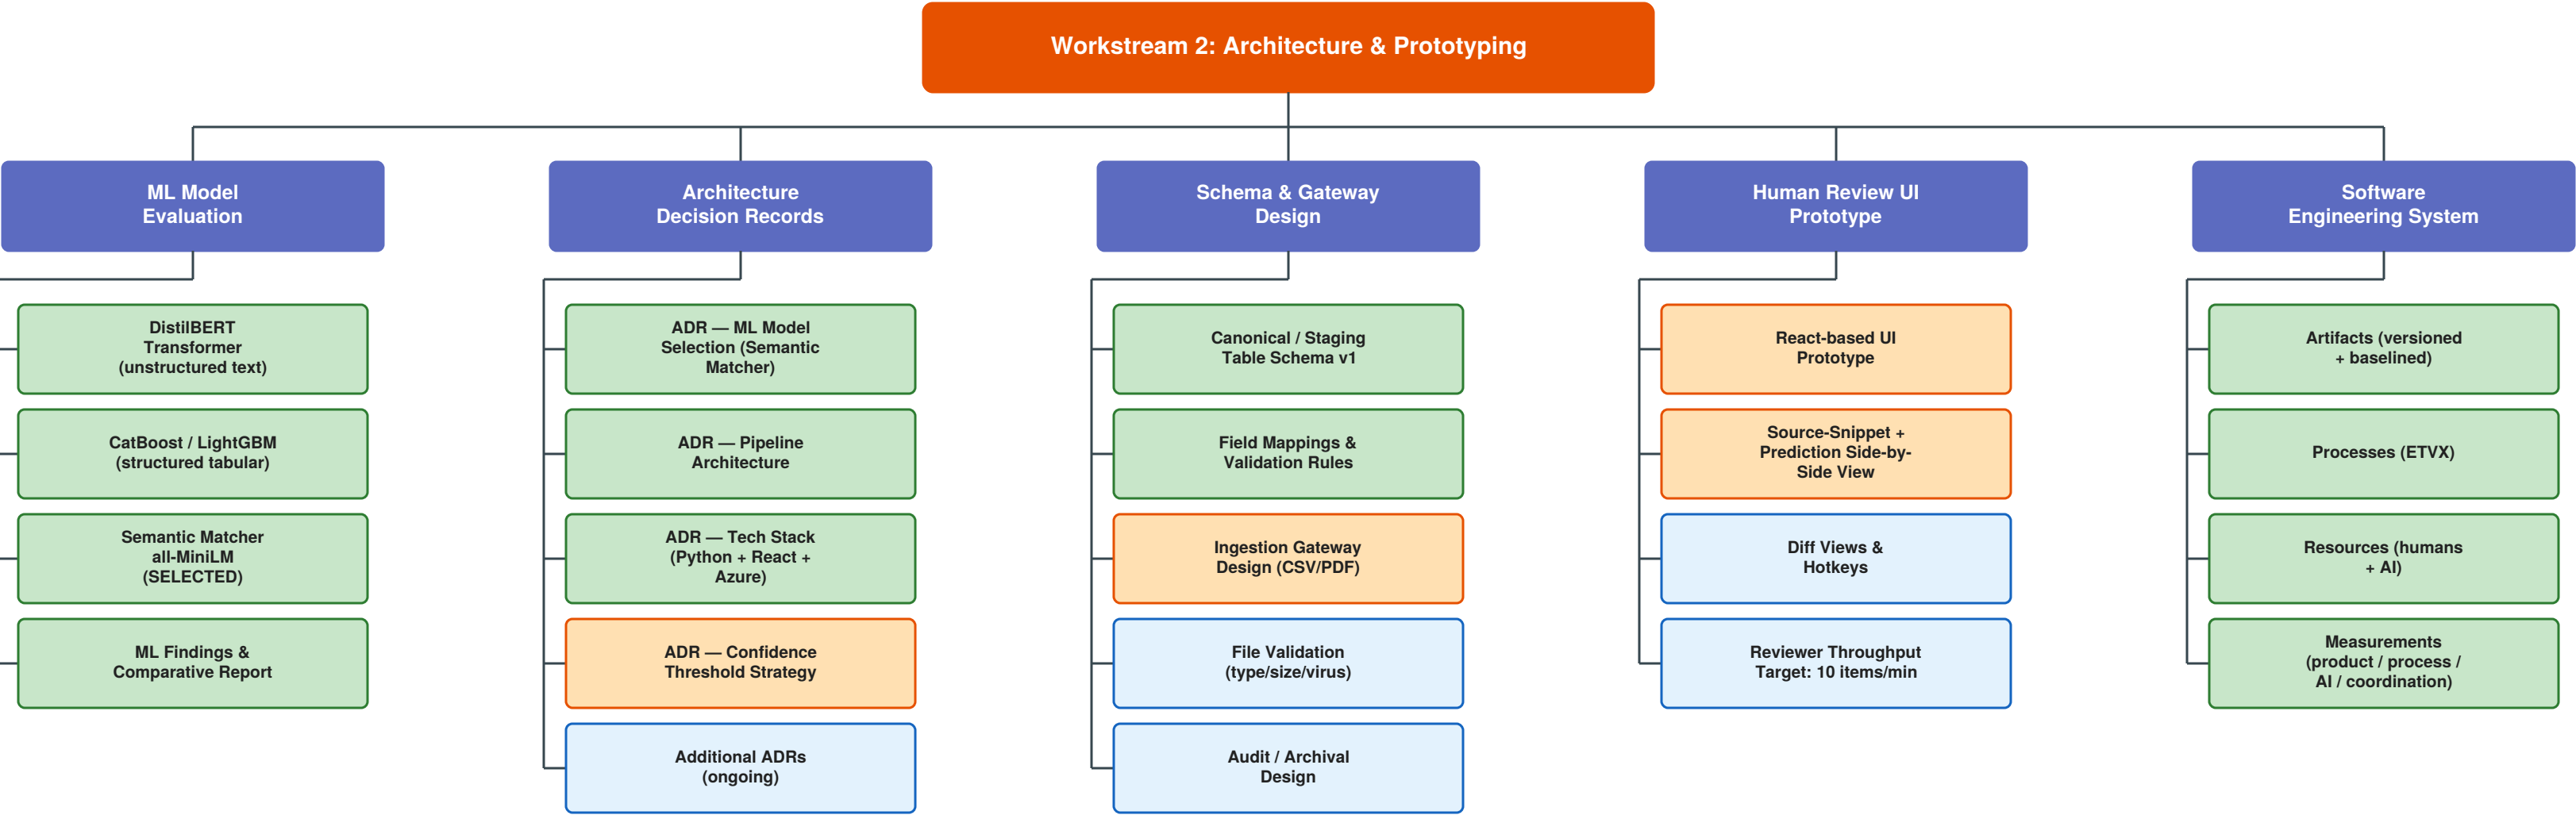

Project Timeline — context for this workstream


| Spring 2026<br>Jan 22 – May 11         |                                       |                                                                   |                                                                |                                                 | Summer 2026<br>May 18 – Aug 8           |                                                   |                                                   |                                                 | Fall 2026<br>Aug 24 – Dec 11                     |                                        |                                                |                                        |
|----------------------------------------|---------------------------------------|-------------------------------------------------------------------|----------------------------------------------------------------|-------------------------------------------------|-----------------------------------------|---------------------------------------------------|---------------------------------------------------|-------------------------------------------------|--------------------------------------------------|----------------------------------------|------------------------------------------------|----------------------------------------|
| P1: Discovery + SES<br>Feb 18 – Feb 27 | P2: Reqs + Arch v1<br>Feb 28 – Mar 17 | P3: Vertical Slice 1<br>Ingestion → Normalized<br>Mar 18 – Mar 31 | P4: Vertical Slice 2<br>Prediction + Routing<br>Apr 1 – Apr 14 | P5: Hardening + Critique Demo<br>Apr 15 – May 1 | P6: Wrap + Evaluations<br>May 2 – May 4 | Core Pipeline Development (WS3)<br>Full Build-Out | ML Service + Integrations<br>Attribute Prediction | CRIT 2: Summer End-of-Semester<br>End of Summer | Integration + E2E Testing (WS4)<br>Full Pipeline | Pilot Deployment (UAT)<br>Sandbox Env. | Knowledge Transfer + Handoff<br>Final Delivery | CRIT 3: Final Delivery<br>Dec 11, 2026 |

WS2 spans Spring (ML evaluation, ADRs, SES) and continues into Summer (full Ingestion Gateway design + Human Review UI).

WS3 — Core Pipeline Development

Summer 2026 → Fall 2026 · Status: Future Work (vertical slice prototypes done in Spring)

Legend: Completed In Progress Future Work

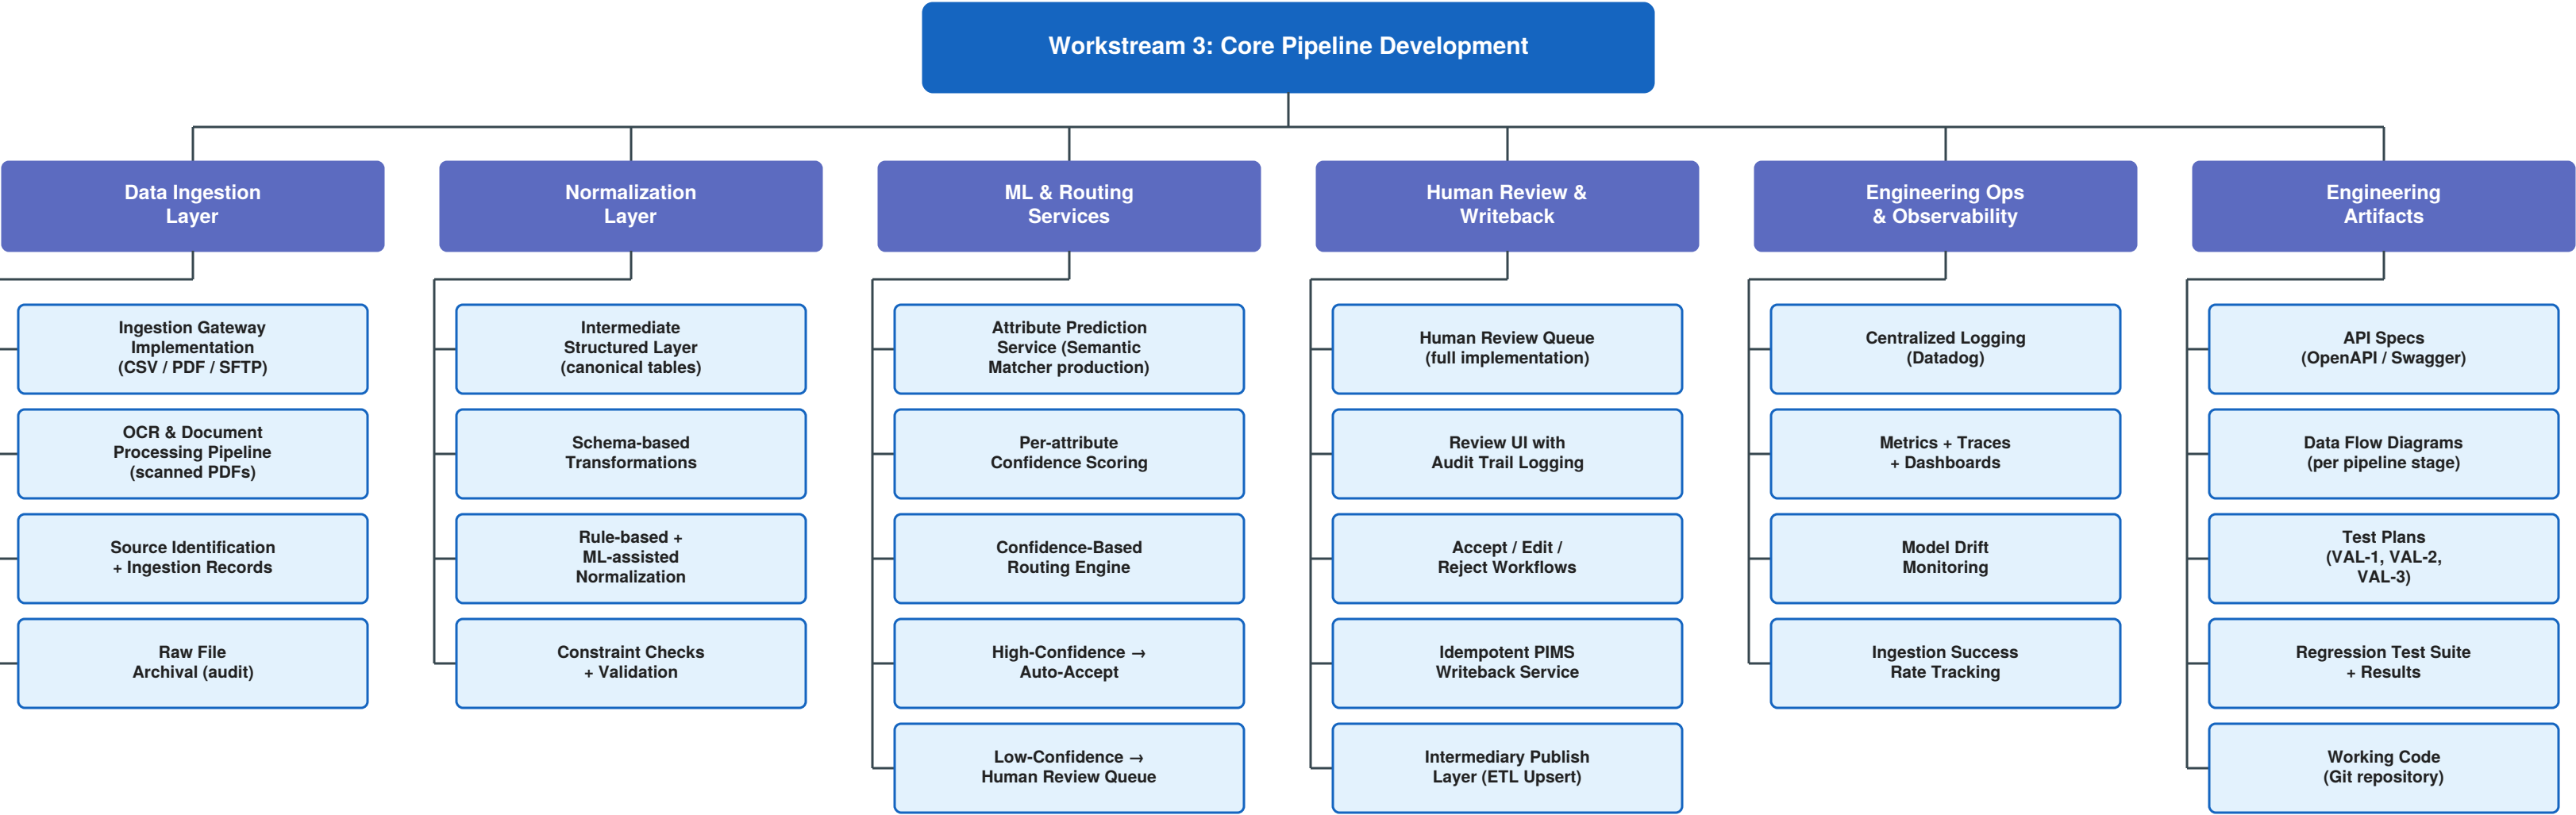

Project Timeline — context for this workstream


| Spring 2026<br>Jan 22 – May 11         |                                       |                                                                   |                                                                |                                                 | Summer 2026<br>May 18 – Aug 8           |                                                   |                                                   |                                                 | Fall 2026<br>Aug 24 – Dec 11                     |                                        |                                                |                                        |
|----------------------------------------|---------------------------------------|-------------------------------------------------------------------|----------------------------------------------------------------|-------------------------------------------------|-----------------------------------------|---------------------------------------------------|---------------------------------------------------|-------------------------------------------------|--------------------------------------------------|----------------------------------------|------------------------------------------------|----------------------------------------|
| P1: Discovery + SES<br>Feb 18 – Feb 27 | P2: Reqs + Arch v1<br>Feb 28 – Mar 17 | P3: Vertical Slice 1<br>Ingestion → Normalized<br>Mar 18 – Mar 31 | P4: Vertical Slice 2<br>Prediction + Routing<br>Apr 1 – Apr 14 | P5: Hardening + Critique Demo<br>Apr 15 – May 1 | P6: Wrap + Evaluations<br>May 2 – May 4 | Core Pipeline Development (WS3)<br>Full Build-Out | ML Service + Integrations<br>Attribute Prediction | CRIT 2: Summer End-of-Semester<br>End of Summer | Integration + E2E Testing (WS4)<br>Full Pipeline | Pilot Deployment (UAT)<br>Sandbox Env. | Knowledge Transfer + Handoff<br>Final Delivery | CRIT 3: Final Delivery<br>Dec 11, 2026 |

WS3 is the largest workstream — full system build-out happens primarily in Summer 2026 (2,160 team-hours allocated).

WS4 — Integration, Testing & Pilot Deployment

Fall 2026 (Aug 24 – Dec 11) · Status: Future Work — Final Delivery target Nov/Dec 2026

Legend: Completed In Progress Future Work

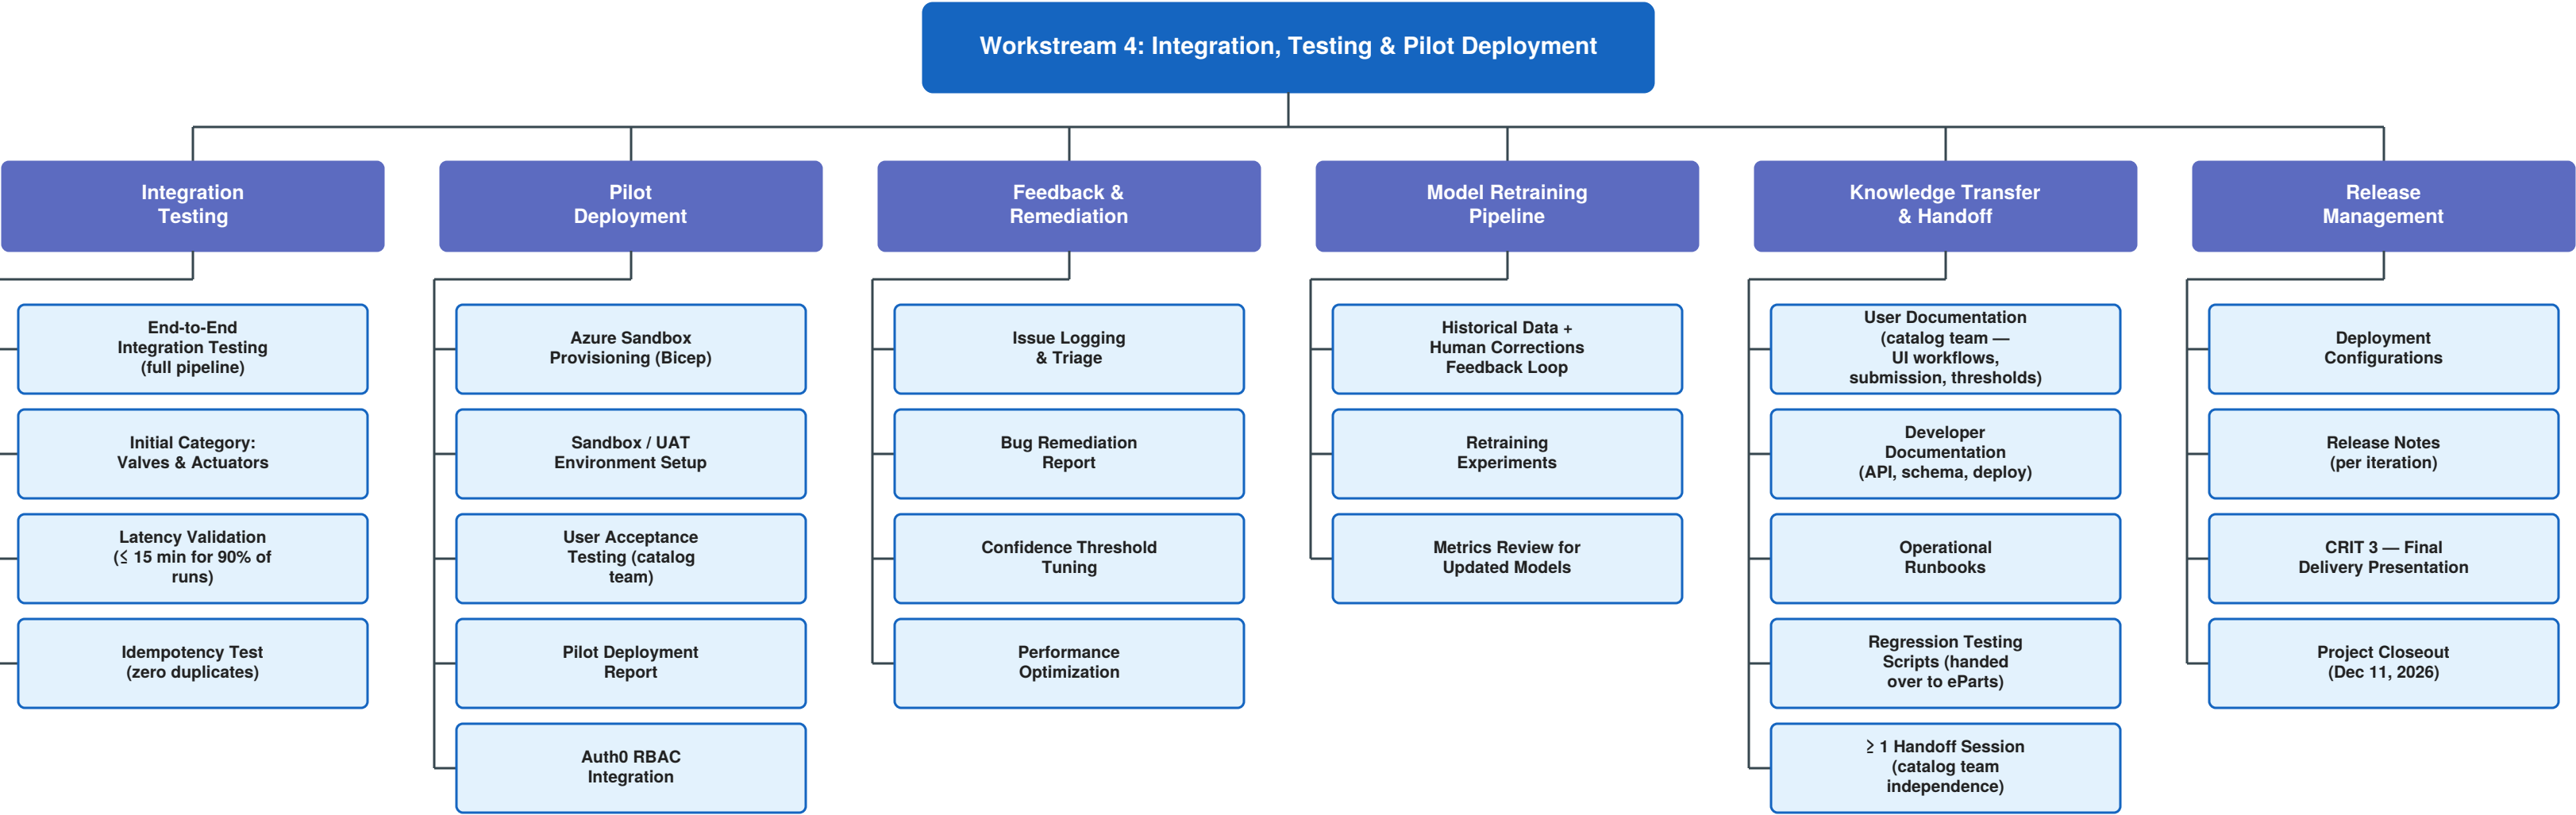

Project Timeline — context for this workstream


| Spring 2026<br>Jan 22 – May 11         |                                       |                                                                   |                                                                |                                                 | Summer 2026<br>May 18 – Aug 8           |                                                   |                                                   |                                                 | Fall 2026<br>Aug 24 – Dec 11                     |                                        |                                                |                                        |
|----------------------------------------|---------------------------------------|-------------------------------------------------------------------|----------------------------------------------------------------|-------------------------------------------------|-----------------------------------------|---------------------------------------------------|---------------------------------------------------|-------------------------------------------------|--------------------------------------------------|----------------------------------------|------------------------------------------------|----------------------------------------|
| P1: Discovery + SES<br>Feb 18 – Feb 27 | P2: Reqs + Arch v1<br>Feb 28 – Mar 17 | P3: Vertical Slice 1<br>Ingestion → Normalized<br>Mar 18 – Mar 31 | P4: Vertical Slice 2<br>Prediction + Routing<br>Apr 1 – Apr 14 | P5: Hardening + Critique Demo<br>Apr 15 – May 1 | P6: Wrap + Evaluations<br>May 2 – May 4 | Core Pipeline Development (WS3)<br>Full Build-Out | ML Service + Integrations<br>Attribute Prediction | CRIT 2: Summer End-of-Semester<br>End of Summer | Integration + E2E Testing (WS4)<br>Full Pipeline | Pilot Deployment (UAT)<br>Sandbox Env. | Knowledge Transfer + Handoff<br>Final Delivery | CRIT 3: Final Delivery<br>Dec 11, 2026 |



Project Management — Cross-Cutting Activities

Continuous (Jan 22, 2026 – Dec 11, 2026) · Status: Ongoing throughout the project

Legend: Completed In Progress Future Work

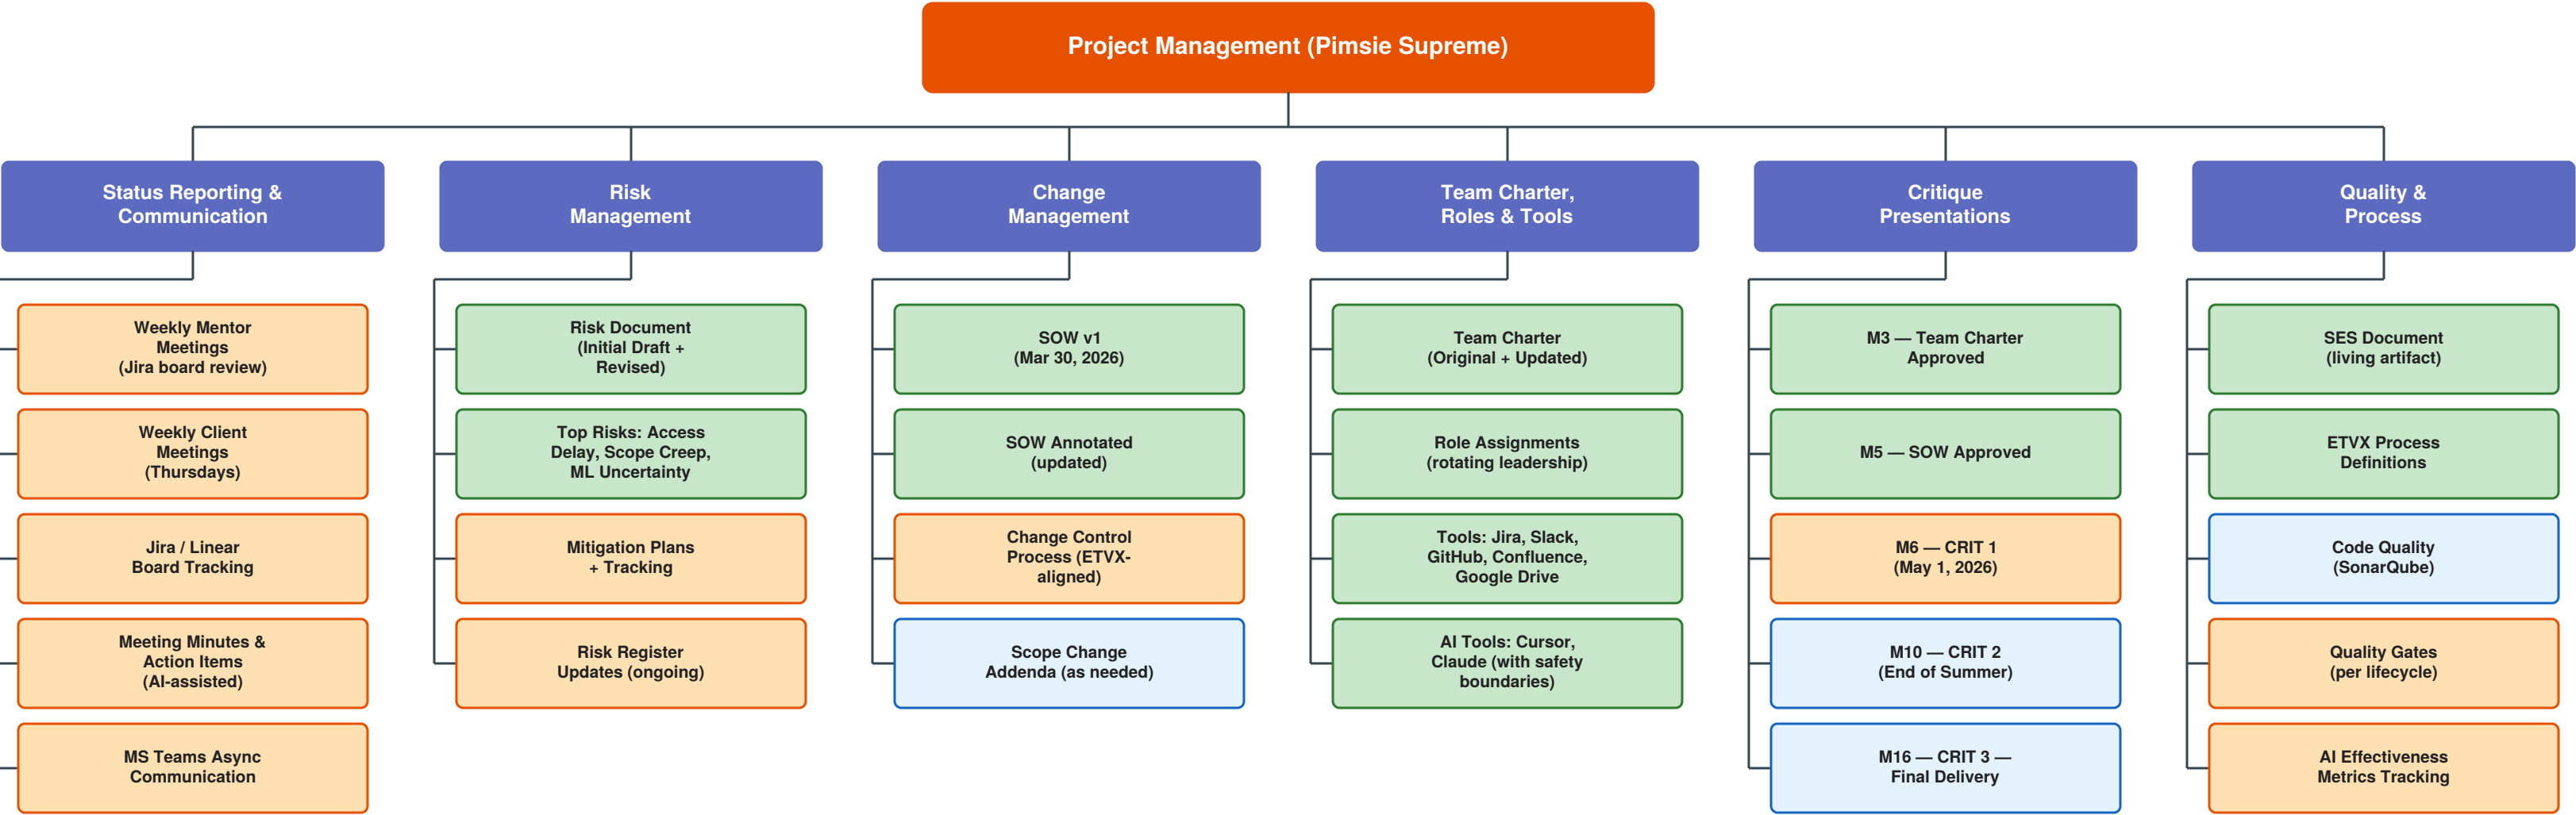

Project Timeline — context for this workstream

| Spring 2026<br>Jan 22 – May 11         |                                       |                                                                |                                                             |                                                 | Summer 2026<br>May 18 – Aug 8           |                                                   |                                                   |                                                 | Fall 2026<br>Aug 24 – Dec 11                     |                                        |                                                |                                        |
|----------------------------------------|---------------------------------------|----------------------------------------------------------------|-------------------------------------------------------------|-------------------------------------------------|-----------------------------------------|---------------------------------------------------|---------------------------------------------------|-------------------------------------------------|--------------------------------------------------|----------------------------------------|------------------------------------------------|----------------------------------------|
| P1: Discovery + SES<br>Feb 18 – Feb 27 | P2: Reqs + Arch v1<br>Feb 28 – Mar 17 | P3: Vertical Slice 1 Ingestion → Normalized<br>Mar 18 – Mar 31 | P4: Vertical Slice 2 Prediction + Routing<br>Apr 1 – Apr 14 | P5: Hardening + Critique Demo<br>Apr 15 – May 1 | P6: Wrap + Evaluations<br>May 2 – May 4 | Core Pipeline Development (WS3)<br>Full Build-Out | ML Service + Integrations<br>Attribute Prediction | CRIT 2: Summer End-of-Semester<br>End of Summer | Integration + E2E Testing (WS4)<br>Full Pipeline | Pilot Deployment (UAT)<br>Sandbox Env. | Knowledge Transfer + Handoff<br>Final Delivery | CRIT 3: Final Delivery<br>Dec 11, 2026 |

Project Management is a cross-cutting workstream that runs continuously across all semesters.
